


Figure 12.4 Order Form

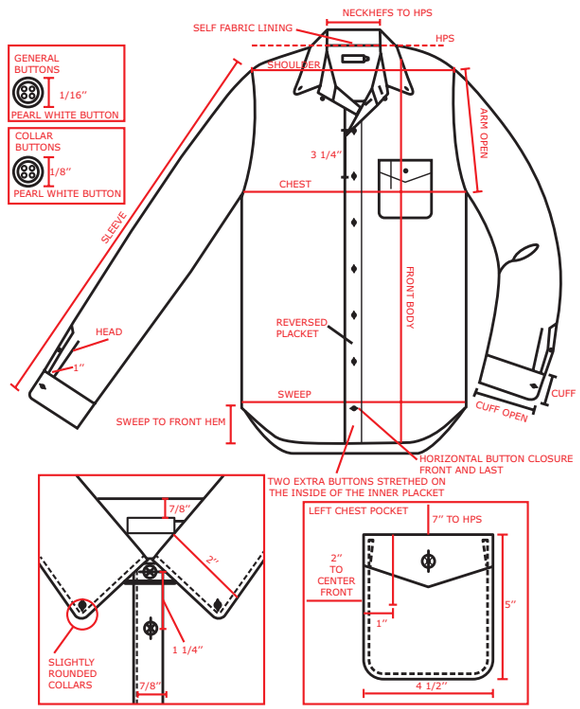


Figure 12.5 Specification Details

12.6.7 The Process of Order Review

Order review is going through or reading the order sheet carefully to check for the particulars with that of enquiry for any variations and also requirements of the particular order.

The order sheet have details like the quality requirements, packing details and accessories details. The merchandiser must check the quality, requirements and note down the important instruction regarding label placement , wash care and spelling of words. Any discrepancies in the order sheet should be informed to the buyer at the initial stage itself and should be corrected before the commencement of the production. This is an important activity which would help in efficient and effective follow up and execution of the order.

12.6.8 Planning and Programming

Planning includes the time calculation and scheduling of the order lead time. Planning include master planning and scheduling or critical path. Programming involves decision making on certain activities in a particular order.

Master Planning

The total time required to complete the order is estimated. If not necessary alternatives to execute the order in time is also planned. The target date for shipment is set before master planning. The target date is normally set one week to ten days earlier than the delivery date mentioned in the order sheet. Yarn purchasing, fabric production, processing, cutting, sewing, checking, ironing, packing, final inspection and shipment departments need to be consulted regularly to know the progress of all these activities. Their available capacity details should also be noted. If the final inspection date falls on the target date then the order can be shipped in given time. If not, then the revised planning should be done by outsourcing or increasing the capacity levels for various activities.

XII TDD_English version CHAPTER 12.indd 186 1/13/2020 3:38:05 PM
